



2015 Street Improvements

Weekly Construction Newsletter

Highland, Marsh, Skyline, Grainwood, Eau Claire

Construction Includes:

- *New sanitary sewer main and service lines*
- *New water main and service lines*
- *New storm sewer*
- *New street pavement*
- *Intersection street lights*
- *Driveway and turf restoration*

Construction Complete:

- *Substantial: November 15, 2015*
- *Final: July 1, 2016*



Roger Ness
 Construction Observer
 Cell Phone: 612-845-8093
 E-mail: rogerne@bolton-menk.com

Cory Bienfang, P.E.
 Project Engineer
 Cell: 507-995-2936
 E-mail: corybi@bolton-menk.com

PROJECT UPDATE

MARSH STREET


The Contractor successfully completed the installation of the base lift of the new bituminous pavement today. This is how the roadway will remain until next summer at which time the final lift of bituminous pavement will be installed. The restoration of the remaining driveways is planned for next week and final confirmation on private driveway replacements is requested by Monday morning, June 1st. The final boulevard grading and sodding is not scheduled at this time to allow the private utilities to complete their work, which is planned to begin next week.

GRAINWOOD CIRCLE

The Contractor has completed the installation of the services along the south and east legs of Grainwood Circle. The only remaining utility work along these legs is the new storm sewer, which the Contractor started yesterday and is expected to complete early next week. Once the storm sewer is completed the Contractor plans to continue with the installation of the new sanitary sewer and watermain on the west and north legs of Grainwood Circle. The Contractor plans to start with the new sanitary sewer on the north leg first.

HIGHLAND/SKYLINE

The Contractor is expecting to begin Stage 1B that consists of the south portion of Highland Avenue and the cul-de-sac on Skyline Avenue the week of June 8th. A more accurate estimate will be provided next week, but in preparation for the start of actual construction, the Contractor plans to start laying out the temporary water main within this area next week.

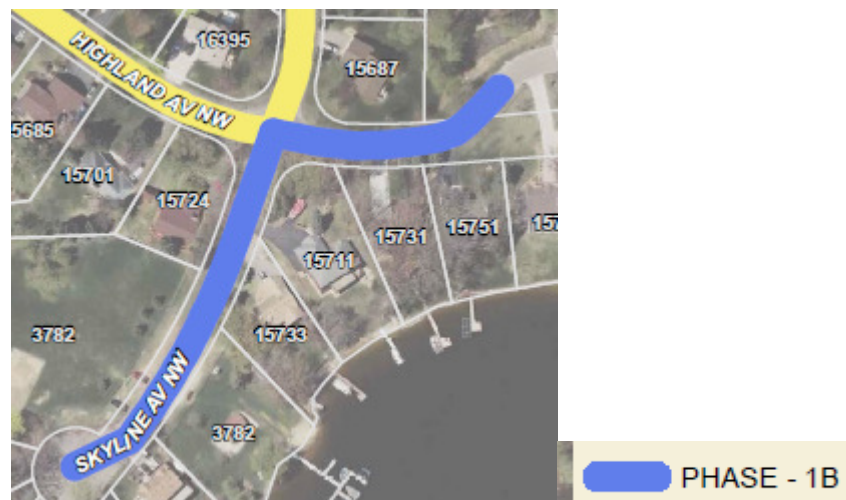

As a reminder the City approved hours of construction operation are 7:00 am to 7:00 pm, during which time access through the specific work area may be restricted.

Please contact me at 507-995-2936 or corybi@bolton-menk.com if you have any additional questions relating this update or the project overall.
