



2015 Street Improvements

Highland, Marsh, Skyline, Grainwood, Eau Claire

Weekly Construction Newsletter

Construction Includes:

- New sanitary sewer main and service lines
- New water main and service lines
- New storm sewer
- New street pavement
- Intersection street lights
- Driveway and turf restoration

Construction Complete:

- Substantial:
November 15, 2015
- Final:
July 1, 2016



Roger Ness
Construction Observer
Cell Phone: 612-845-8093
E-mail: rogerne@bolton-menk.com

Cory Bienfang, P.E.
Project Engineer
Cell: 507-995-2936
E-mail: corybi@bolton-menk.com

PROJECT UPDATE

MARSH STREET

The private utility work has yet to be completed and they have requested to hold off the remaining driveway restorations until after the completion of their planned work.


GRAINWOOD CIRCLE

The Contractor has completed the installation of all new underground utility work within the west, south and east legs of Grainwood Circle. The remaining utility work within the north leg is progressing with plan to have sanitary sewer completed by mid-week next week and watermain planned to be completed by the end of the week if actual construction progresses really well. The new sanitary sewer and water services would be completed the week of June 15th.

The Contractor is continuing at the same time with the roadway construction, with focus to have the south leg completed with the new aggregate base before the weekend. Then next week the Contractor plans to continue with the construction of the roadway on the east and west legs starting with the excavation and continuing with the installation of the new sand and aggregate base.

HIGHLAND/SKYLINE

The Contractor is expecting to begin Stage 1B that consists of the south portion of Highland Avenue and the cul-de-sac on Skyline Avenue the week of June 15th. The Contractor plans to start laying out the temporary water main within this area next week.

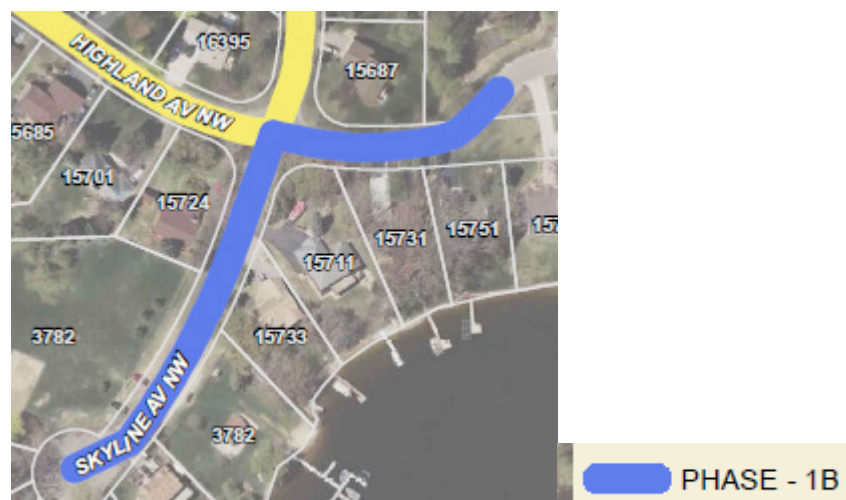

As a reminder the City approved hours of construction operation are 7:00 am to 7:00 pm, during which time access through the specific work area may be restricted.

Please contact me at 507-995-2936 or corybi@bolton-menk.com if you have any additional questions relating this update or the project overall.
